


DRAFT, SUBJECT TO REVISION - August 6, 2018
 ROC on LTO - August 2019 - DRAFT Schedule

ID	Task Name	Duration	Start	Finish
1	Long-term Re-Operation	446 days	Thu 1/4/18	Thu 9/19/19
2	Brainstorming Workshops	180 days	Thu 1/4/18	Wed 9/12/18
3	NEPA Compliance	266 days	Thu 9/13/18	Thu 9/19/19
4	Alternatives Development	40 days	Thu 9/13/18	Wed 11/7/18
5	Initial Alternative Development and Modeling	10 days	Thu 9/13/18	Wed 9/26/18
6	Analytical Tools List	5 days	Thu 9/13/18	Wed 9/19/18
7	Draft Proposed Action	10 days	Thu 9/27/18	Wed 10/10/18
8	DC Review of Action	5 days	Thu 10/11/18	Wed 10/17/18
9	Modeling and Analysis	20 days	Thu 10/11/18	Wed 11/7/18
10	Draft Alternatives TM	20 days	Thu 9/27/18	Wed 10/24/18
11	Final Alternatives TM	10 days	Thu 10/25/18	Wed 11/7/18
12	Admin Draft EIS	75 days	Thu 11/8/18	Wed 2/20/19
13	Impact Analysis	20 days	Thu 11/8/18	Wed 12/5/18
14	Draft Cumulative Effects Method TM	10 days	Thu 12/6/18	Wed 12/19/18
15	Draft Mitigation Measures TM	10 days	Thu 12/6/18	Wed 12/19/18
16	DC - NOI & EIS Dev Briefing	5 days	Thu 12/20/18	Wed 12/26/18
17	Prepare & Publish NOI	10 days	Thu 12/27/18	Wed 1/9/19
18	Public Scoping	30 days	Thu 1/10/19	Wed 2/20/19
19	Prepare document	15 days	Thu 12/20/18	Wed 1/9/19
20	DC Red Flag Impact Review	5 days	Thu 1/10/19	Wed 1/16/19
21	Cooperating Agency Review	10 days	Thu 1/17/19	Wed 1/30/19
22	Public Draft EIS and Review Period	71 days	Thu 1/31/19	Thu 5/9/19
23	Prepare Public Draft EIS	15 days	Thu 1/31/19	Wed 2/20/19
24	Reclamation Red Flag Review	5 days	Thu 2/21/19	Wed 2/27/19
25	Incorporate Comments	5 days	Thu 2/28/19	Wed 3/6/19
26	NOA Review by DC and Briefing	10 days	Thu 3/7/19	Wed 3/20/19
27	Publish Draft EIS	1 day	Thu 3/21/19	Thu 3/21/19
28	Public Hearings and Public Comment Period	35 days	Fri 3/22/19	Thu 5/9/19
29	Final EIS and ROD	95 days	Fri 5/10/19	Thu 9/19/19
30	Respond to Comments	20 days	Fri 5/10/19	Thu 6/6/19
31	Prepare Final EIS	20 days	Fri 6/7/19	Thu 7/4/19

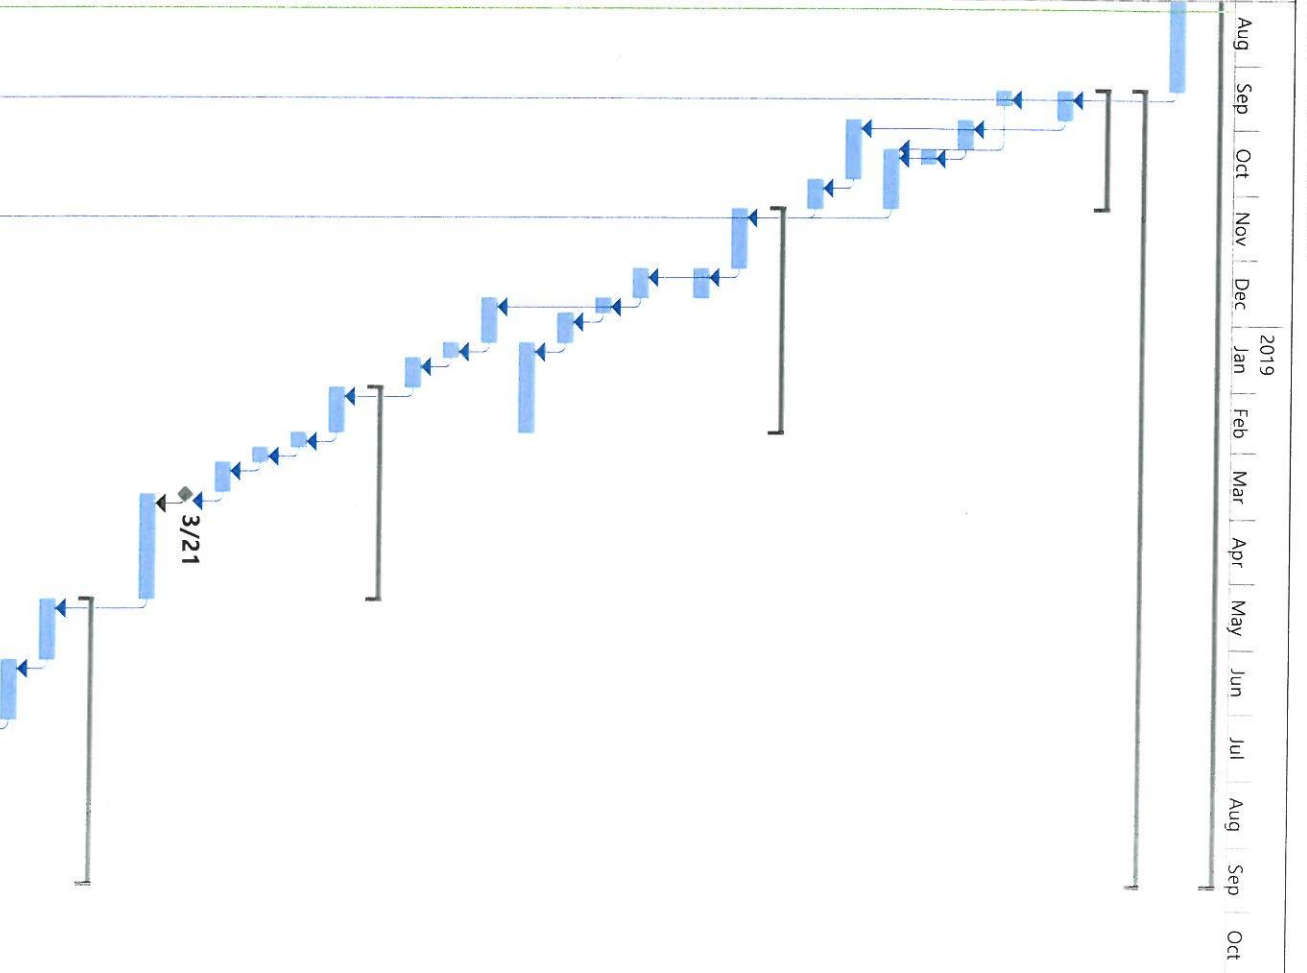

DRAFT, SUBJECT TO REVISION - August 6, 2018
 ROC on LTO - August 2019 - DRAFT Schedule

ID	Task Name	Duration	Start	Finish
32	Reclamation Review	5 days	Fri 7/5/19	Thu 7/11/19
33	Incorporate Comments	10 days	Fri 7/12/19	Thu 7/25/19
34	NOA Review by DC and Briefing	10 days	Fri 7/26/19	Thu 8/8/19
35	Publish Final EIS	1 day	Fri 8/9/19	Fri 8/9/19
36	Wait 30 days	20 days	Mon 8/12/19	Fri 9/6/19
37	Prepare Record of Decision	5 days	Mon 9/9/19	Fri 9/13/19
38	DC Review of ROD	3 days	Mon 9/16/19	Wed 9/18/19
39	Sign Record of Decision	1 day	Thu 9/19/19	Thu 9/19/19
40	Endangered Species Act Compliance	247 days	Thu 9/13/18	Fri 8/23/19
41	Admin Draft BA	95 days	Thu 9/13/18	Wed 1/23/19
42	Draft Introductory Sections	30 days	Thu 9/13/18	Wed 10/24/18
43	Draft Species Accounts	30 days	Thu 10/25/18	Wed 12/5/18
44	Effects Analysis	20 days	Thu 11/8/18	Wed 12/5/18
45	Prepare Admin Draft BA	10 days	Thu 12/6/18	Wed 12/19/18
46	DC, Reclamation, DWR, Agency Review	10 days	Thu 12/20/18	Wed 1/2/19
47	Incorporate Comments	5 days	Thu 1/3/19	Wed 1/9/19
48	DNFR Review	10 days	Thu 1/10/19	Wed 1/23/19
49	Final BA	41 days	Thu 1/24/19	Thu 3/21/19
50	Prepare Final BA	20 days	Thu 1/24/19	Wed 2/20/19
51	DC, Reclamation, and DWR Review	10 days	Thu 2/21/19	Wed 3/6/19
52	Incorporate Comments	10 days	Thu 3/7/19	Wed 3/20/19
53	Submit Final BA to NMFS and USFWS	1 day	Thu 3/21/19	Thu 3/21/19
54	Biological Opinions	111 days	Fri 3/22/19	Fri 8/23/19
55	Draft BOs	95 days	Fri 3/22/19	Thu 8/1/19
56	DC, Reclamation, and Water User Review	5 days	Fri 8/2/19	Thu 8/8/19
57	Revise BO Based on Comments	10 days	Fri 8/9/19	Thu 8/22/19
58	Submit Final BO's to Reclamation	1 day	Fri 8/23/19	Fri 8/23/19

